Test results can tell you what features were tested, but they can't tell you which features have no tests at all. One popular way to achieve this is to integrate the BDD reporting process with a digital product backlog.

11.3 Integrating a digital product backlog

In Agile projects, *task boards* are frequently used to keep track of project activity. A task board is a physical board or wall containing index cards that represent user stories, tasks, bug fixes, and other activities the team must undertake to complete the project. A simple example can be seen in figure 11.6.

The exact layout of a task board is very flexible and is generally different for each team and project, but the general principle is always the same. During an initial planning session, work is broken down into the user stories, tasks, and so on that need to be delivered during the current iteration. Each task or user story goes in a column on the board, based on its status (not started, in progress, done, and so forth). Each day, team members get together in front of the task board to discuss the status of the task they're working on, possibly moving the cards from one column to another. The main advantage of this format is to let the whole team see at a glance what everyone is working on, making it easier to coordinate work and troubleshoot blockages.

Physical boards are excellent communication facilitators, and they provide great visibility for the current work in progress. But they do have their limitations. For example, they aren't optimal for teams that aren't colocated, they can be time-consuming to

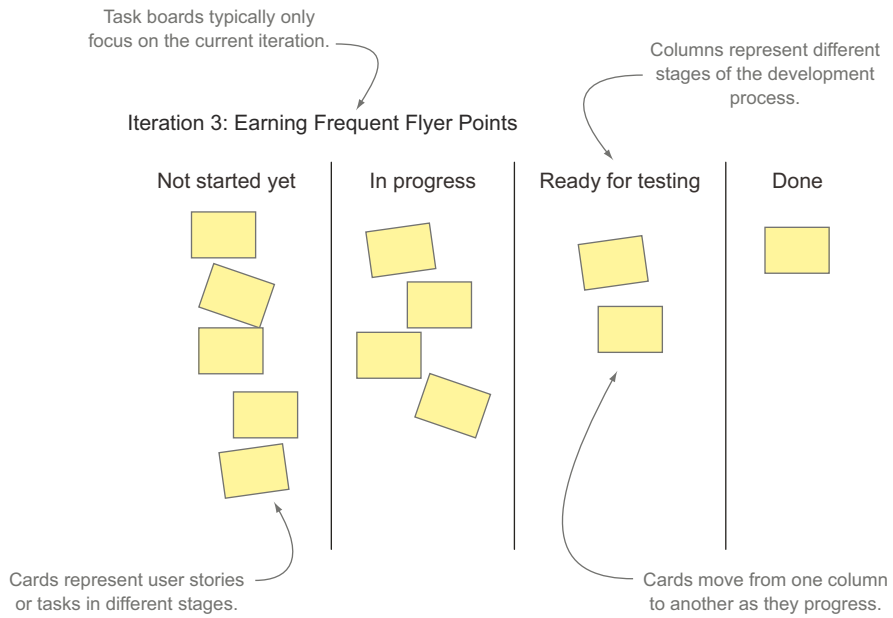


Figure 11.6 A task board is a visual representation of the activities currently going on in a project.
