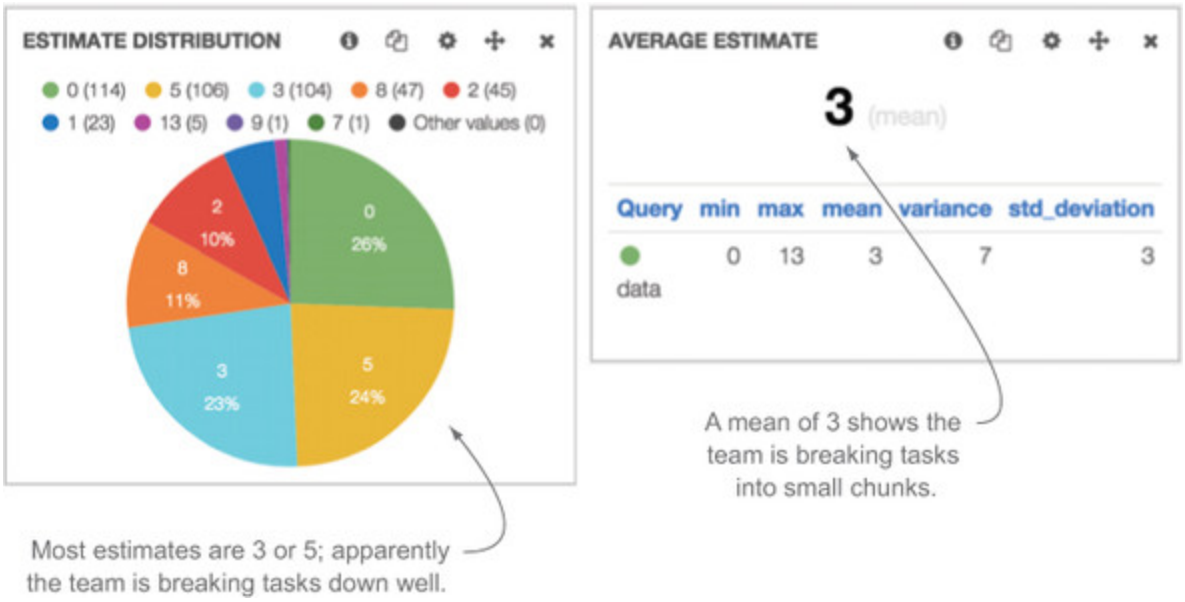


This team is using the Fibonacci series of estimation with a minimum estimate of 1 and a maximum estimate of 13 in a two-week, or 10-working-day, sprint. The potential values in the Fibonacci series are 1, 2, 3, 5, 8, and 13, so an average estimate of 3 is fairly low in the spectrum, which is good. Lower estimates show that tasks have been broken down to a workable level.

Overall estimation data looks pretty good; the team seems to be breaking their tasks into small, manageable chunks. With that in mind, the next questions that arise are these:

- How long do these tasks really take?
- Are our estimations accurate?

Estimating with effort vs. time

Story points are often used to estimate tasks in project tracking systems, but they don’t always have a 1:1 translation to time. For example, 16 story points could mean 9 days of development on one team and it could mean 14 days on another team. No matter how you estimate, you’ll have to translate them to time to figure out if they’re accurate.
