
In this case, based on the estimation system used by the team, tasks estimated at 3 points should take around 2–3 days to complete. The next thing we can pull in is the average amount of time tasks actually take. That is shown in figure 7.8.

Figure 7.8. Adding average time a task takes to get to done. This doesn't look right; an average estimate of 3 should be 2–3 days.

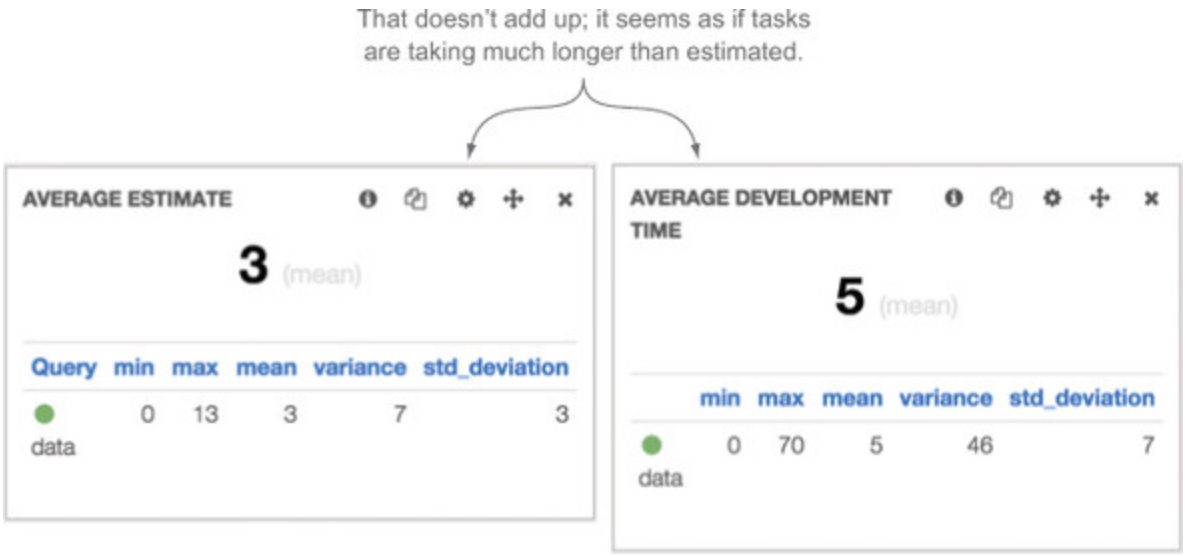

According to our data our average estimate is 3, but on average tasks take 5 days to complete. In this case a sprint is two weeks or 10 working days and the maximum estimate is 13. That would mean that our average estimate should be closer to 8 than 3. The next question that comes to mind is

- Why are tasks taking longer than we think they should?

Because this question is a bit more open-ended we can start by querying for the data that we think doesn't look right to see what properties it has. To do that we can search for all data that has an estimate of 3 and a development time greater than 3 and data that has an estimate of 5 and a development time greater than 5. The query in EC/Lucene looks like this:

```
((devTime:[3 TO *] AND storyPoints:3) OR (devTime:[5 TO *] AND
storyPoints:5))
```
