
managers happy, but that doesn't mean everything is going well on the team. Figure 3.10 is an example of a team that is flat-lining estimates and completion and is also tagging cards as "happy" or "sad" based on how well the developer thought it was done.

Figure 3.10. Estimates and completion mapped with how the developer thought the card was completed

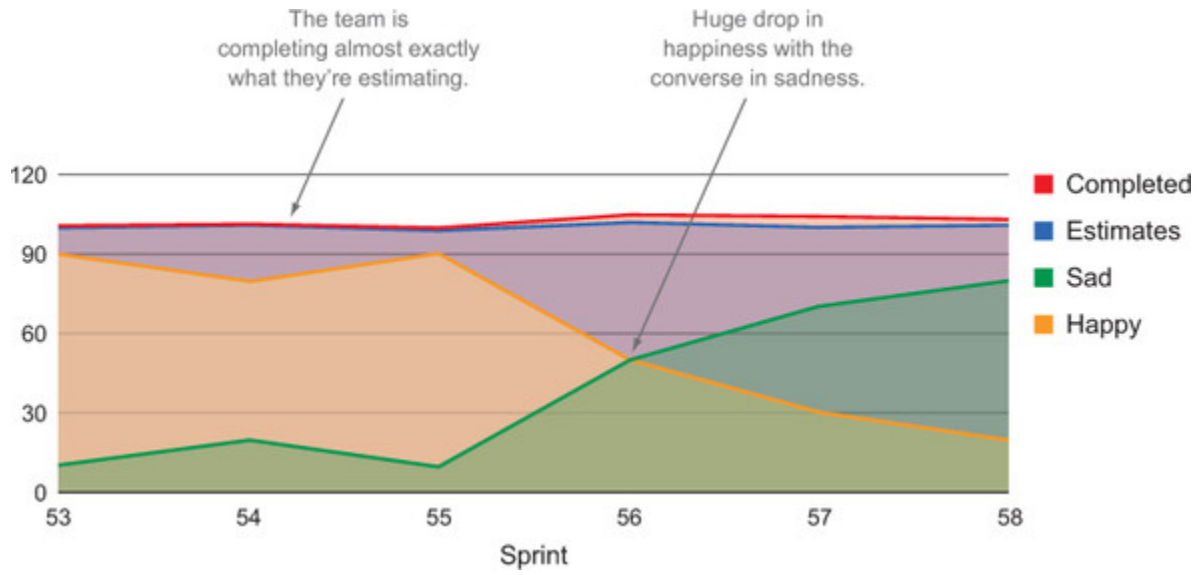

I've seen the chart shown in figure 3.10 on tight deadline projects where a team needed to get an almost unrealistic amount of work done. They started off very happy because they were finishing more than they thought they could and the thrill of it made them feel good. But this lasted for only a few sprints before the team started to get tired. Maybe they were still completing their work, but they weren't as excited about it, and as a result they were tagging their cards as "sad." This is a great example of how additional data can give you real insight into your team outside the normal measurement metrics.

3.3. Key project management metrics; spotting trends in data

Instead of focusing on the typical agile metrics, we'll look at what some key PTS data means when combined. The four metrics we're going to
